

Week 4 & 5

Work Area Building 10

- Large excavation for foundation of Building 10.

Work Area Hus 9

- Building of walls on floor 1.
- Joist work over floor 0, in stages like previous work.
- Refilling soil toward the building.
Removal of facade Building 1 towards Building 9 floor 2 during weeks 4–5.

Work Area Building 1 (Existing Ångström)

- No work planned.

Traffic

- Heavy traffic in connection with construction at Building 9 and excavations at Building 10.

Disturbances

- Heavy traffic.
- Noise from equipment associated with construction.
- Drilling in facade at House 9 for attachment of moulds and insulation. This work will occur primarily outside of normal business hours, but drilling can also occur during daytime. The extent of this work, however, is not more than previous work.
- Refilling of soil toward Building 9 can result in noise and vibrations in Building 1 and Freia.

Closures & Provisional Arrangements

- According to general plan (attached).

Noticeable Apcoming Work (All Start Times are Preliminary)

- Work to remove plaster, insulation of existing walls and attaching moulds for walls facing Building 1 will be done floor-by-floor until the middle of March 2019. Window sections and windows facing the construction will be covered floor-by-floor in connection with the above work.

Construction management for NCC and Akademiska Hus




UPPSALA
UNIVERSITET



AKADEMISKA HUS



Parkeringen avstängd från och med måndag 19/11.

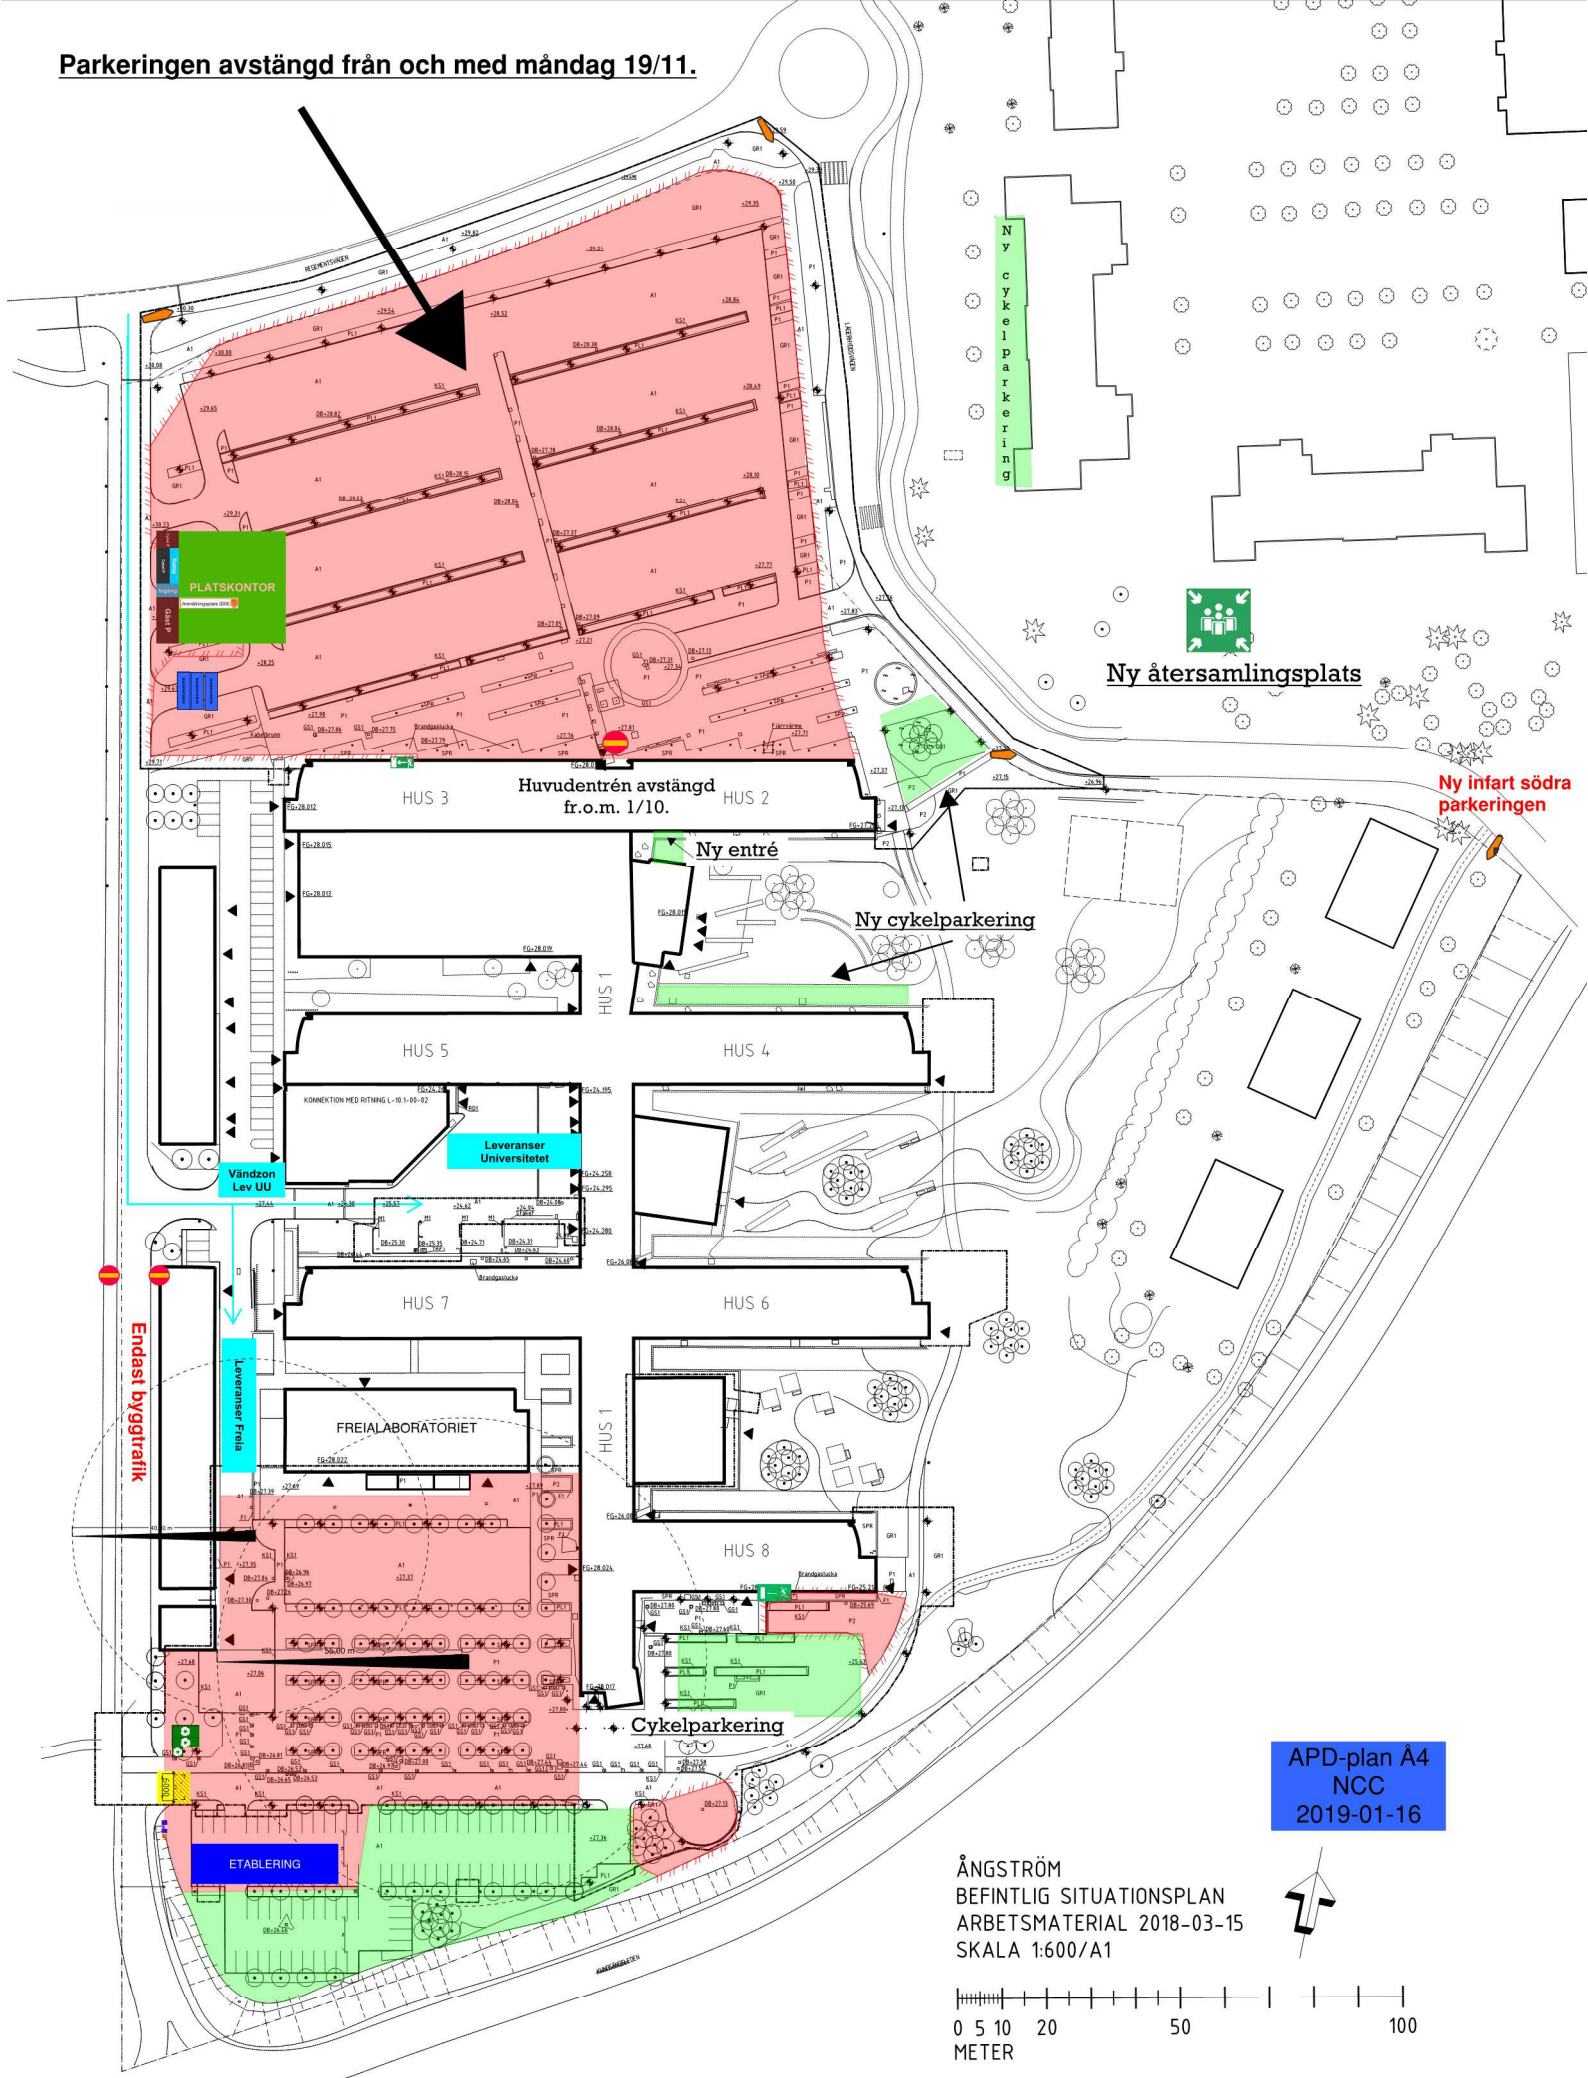

APD-plan Å4
NCC
2019-01-16

ÅNGSTRÖM
BEFINTLIG SITUATIONSPLAN
ARBETSMATERIAL 2018-03-15
SKALA 1:600/A1

